

Terminal 3 Development

Progress Update

7th August 2026

Current Status

Construction Complete

September 2026



Commissioning

August to October 2026



First Sailings

End of October 2026



Project Cost

Within \$493m Budget

(Including circa \$9m for hull strengthening)



Project Progress

Gantry


Progress

► On program



Gantry	Completion
Installation West	Completed
Installation East	Completed
Installation Truss	Completed

- All Gantry modules successfully installed.
- All Linkspans installed.
- Hydraulic system under commission.

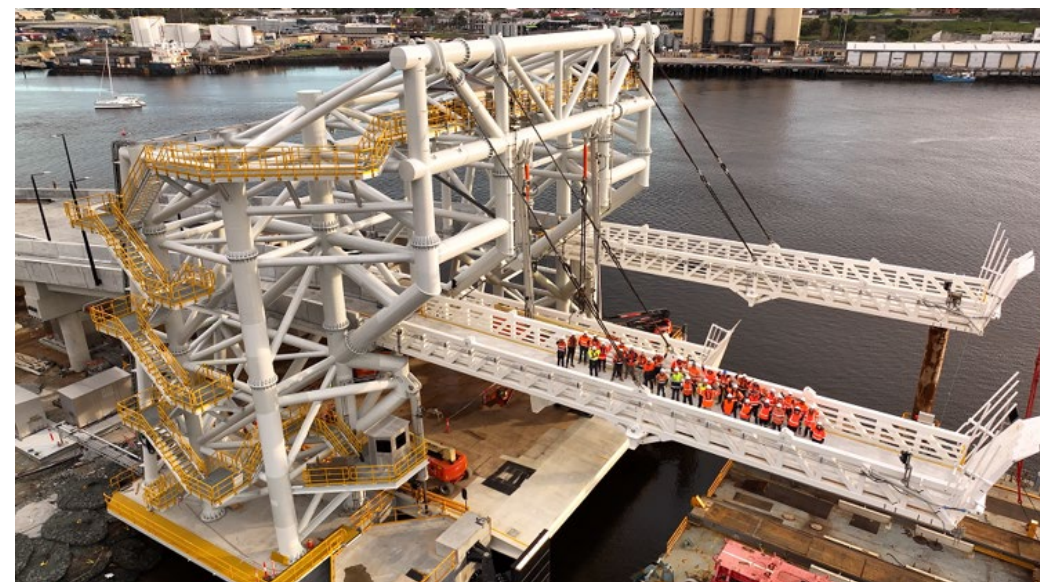

Marine Works

Progress

► On program

Marine Works	Completion
Piling Works	Completed
Fixed Shore (Loading) Ramp	Completed
Land Bollards	Completed
Fender Installation	Completed
Wharf Structures	Completed
AMU Dry Commissioning	Completed

► Fender upgrade to C48 wharf by TasPort has been completed.



Freight Yards

Progress

► On program

Freight Yard	Completion
Freight Entrance and Exit	Completed
Infrastructure	Completed
Asphalt	Completed
Buildings & Equipt.	Completed

- De-mobilisation of site-sheds and line-marking will be completed by the end of September 2026.



Ancillary Buildings

Progress

► On program


Ancillary Buildings	Target Completion
Building 2 - Stevedore & PAX Amenities	14th Aug 2026
Building 3 - Freight Arrival	14th Aug 2026
Building 4 - PAX Check-In Booths	14th Aug 2026
Building 7 - PAX Screening & Exit	14th Aug 2026
Building 8 - Motorbike Shelter	14th Aug 2026



Building 2



Building 3

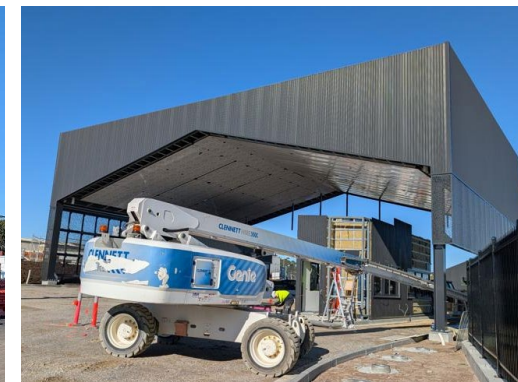

Building 4



Building 7




Building 8

Passenger Boarding

Progress

► On program

Passenger Area	Completion
Entrance Road	Completed
Passenger Check In Booths	14 th Aug 2026
Passenger Marshalling Yard	Completed
Passenger Screening Building	14 th Aug 2026

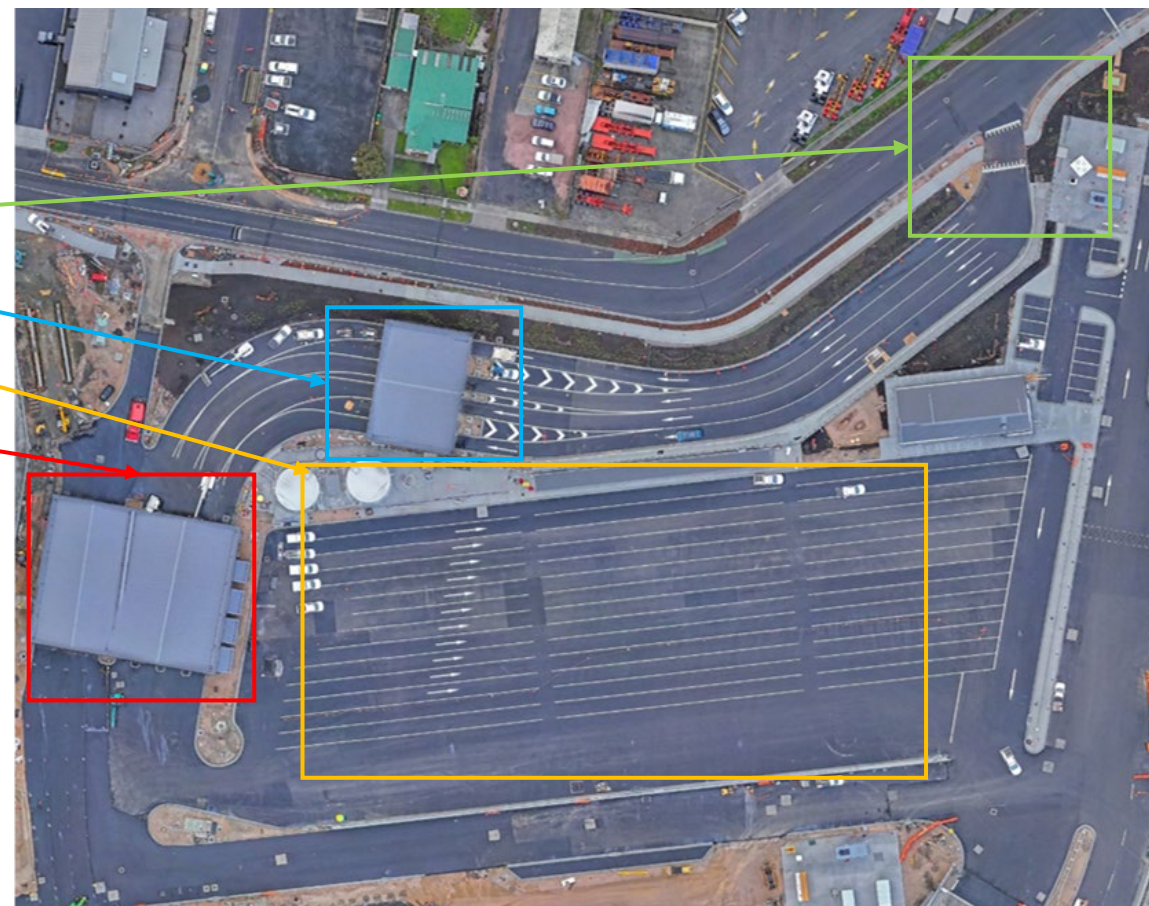


Passenger Terminal

Progress


► On program

Terminal	Completion
Foundations	Completed
Timber Frame	Completed
Weathertight	Completed
Landscaping	21 st Aug 2026
Commissioning	21 st Aug 2026
Completion	30 th Aug 2026

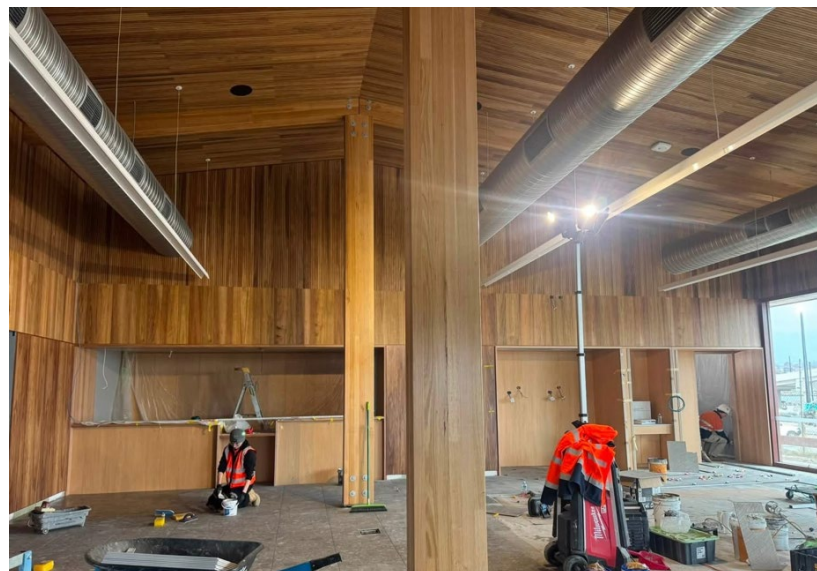


Terminal Commissioning

T3 Commissioning Activities

Work Area	July 2026	August 2026	September 2026	October 2026
Marine / wharf systems				
Truck and car parking & staging				
Buildings				
IT systems proving				
Integrated Testing				
Handover to Operations				

Spirit Operational Readiness Program

Runway to Go-Live

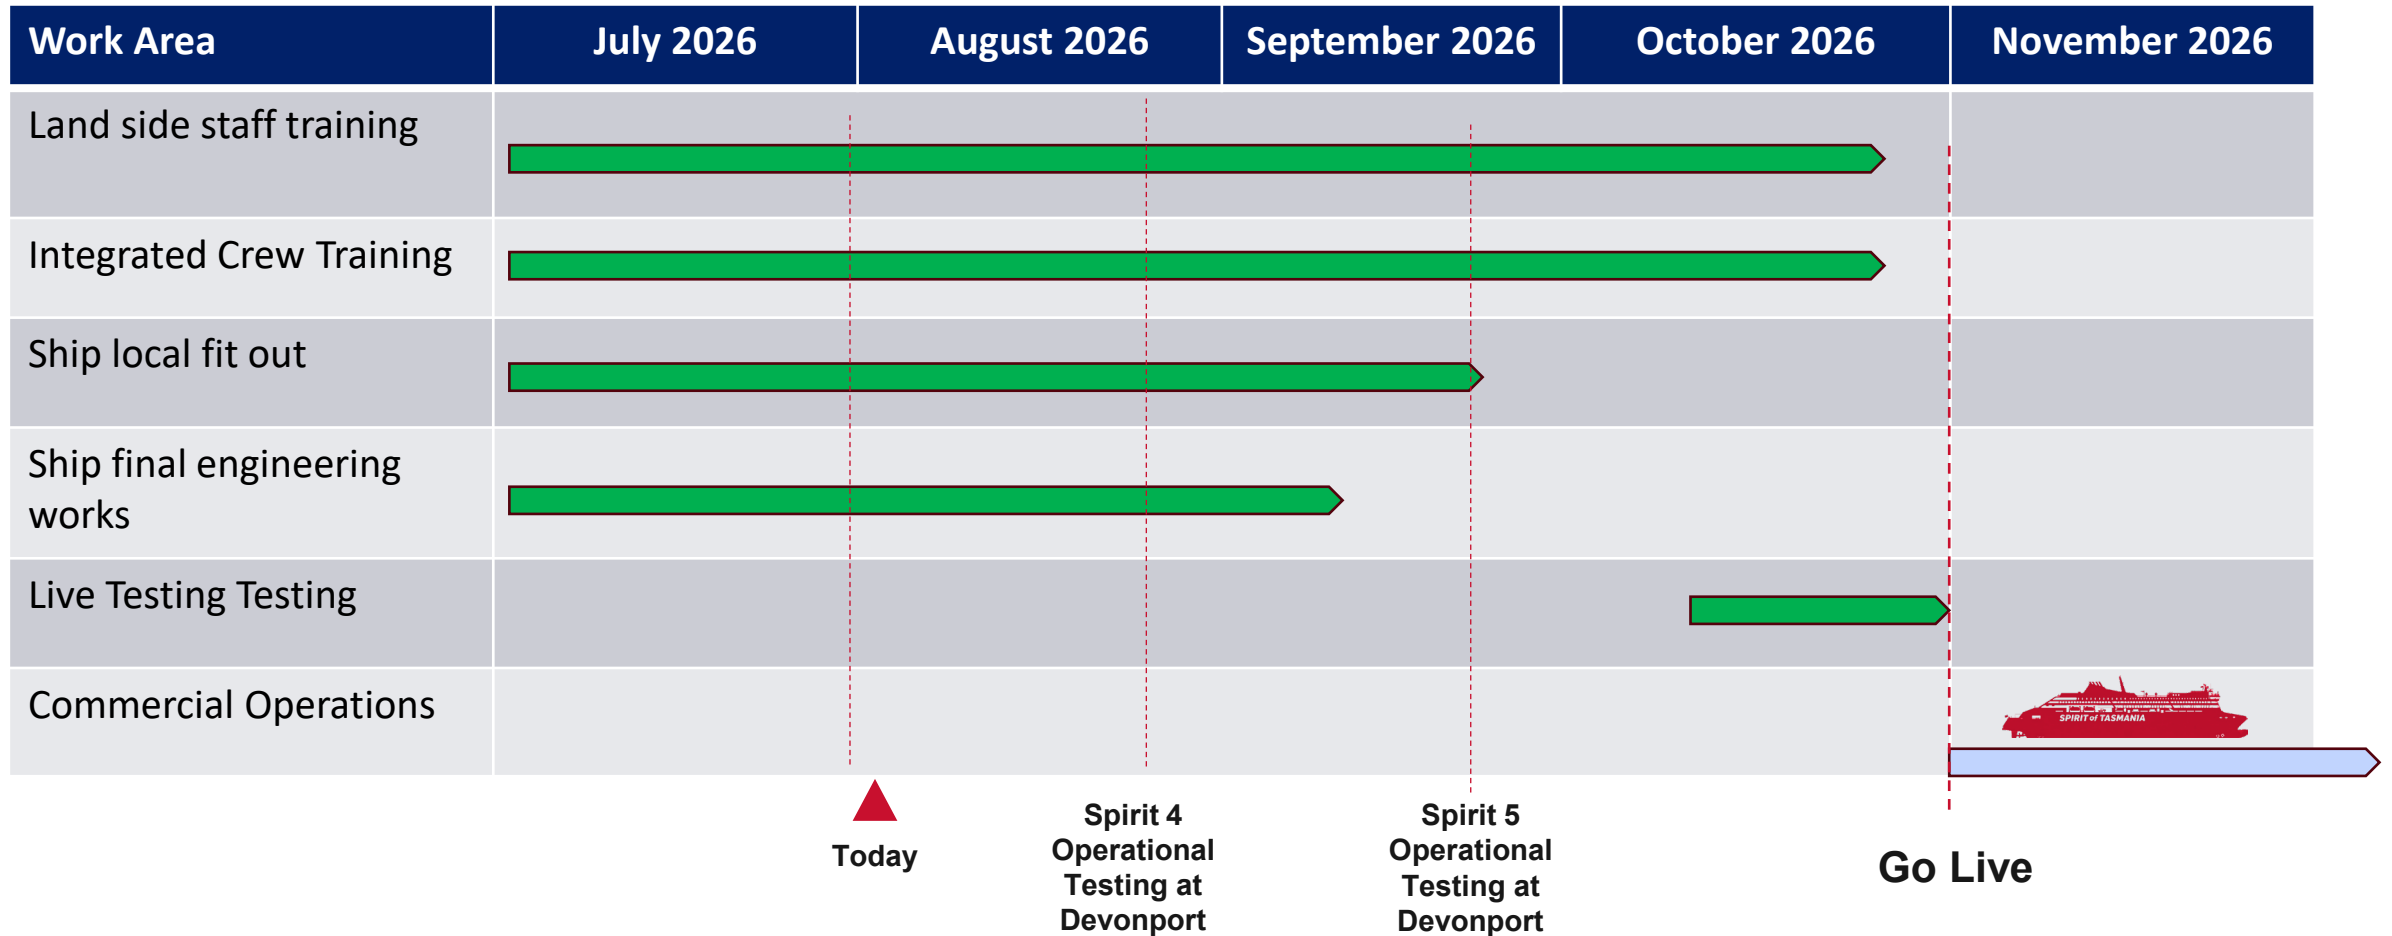

Spirit Operational Readiness Program


Hull Strengthening

Progress > On program

Passenger Area	Completion
Spirit IV strengthening	Completed
Spirit IV insulation	Completed
Spirit V Works	Mid September 2026




Deck 5 – steel work and painting complete

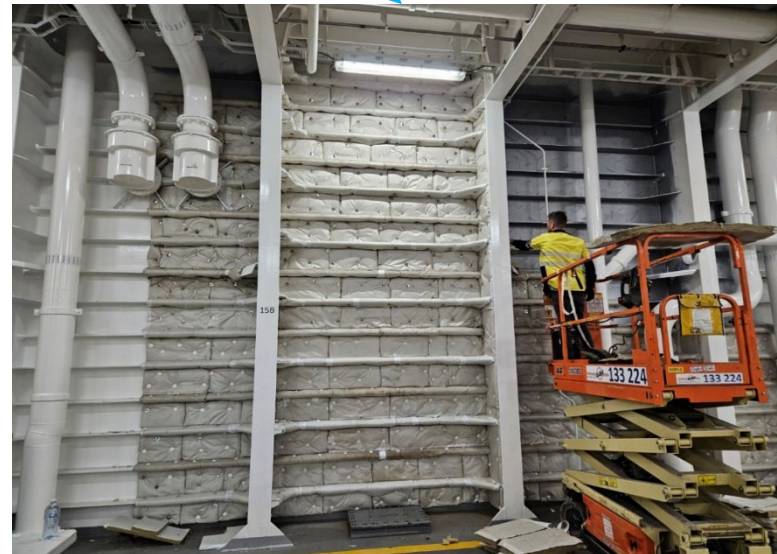

Restoration of A30 insulation

Charting the course to launch

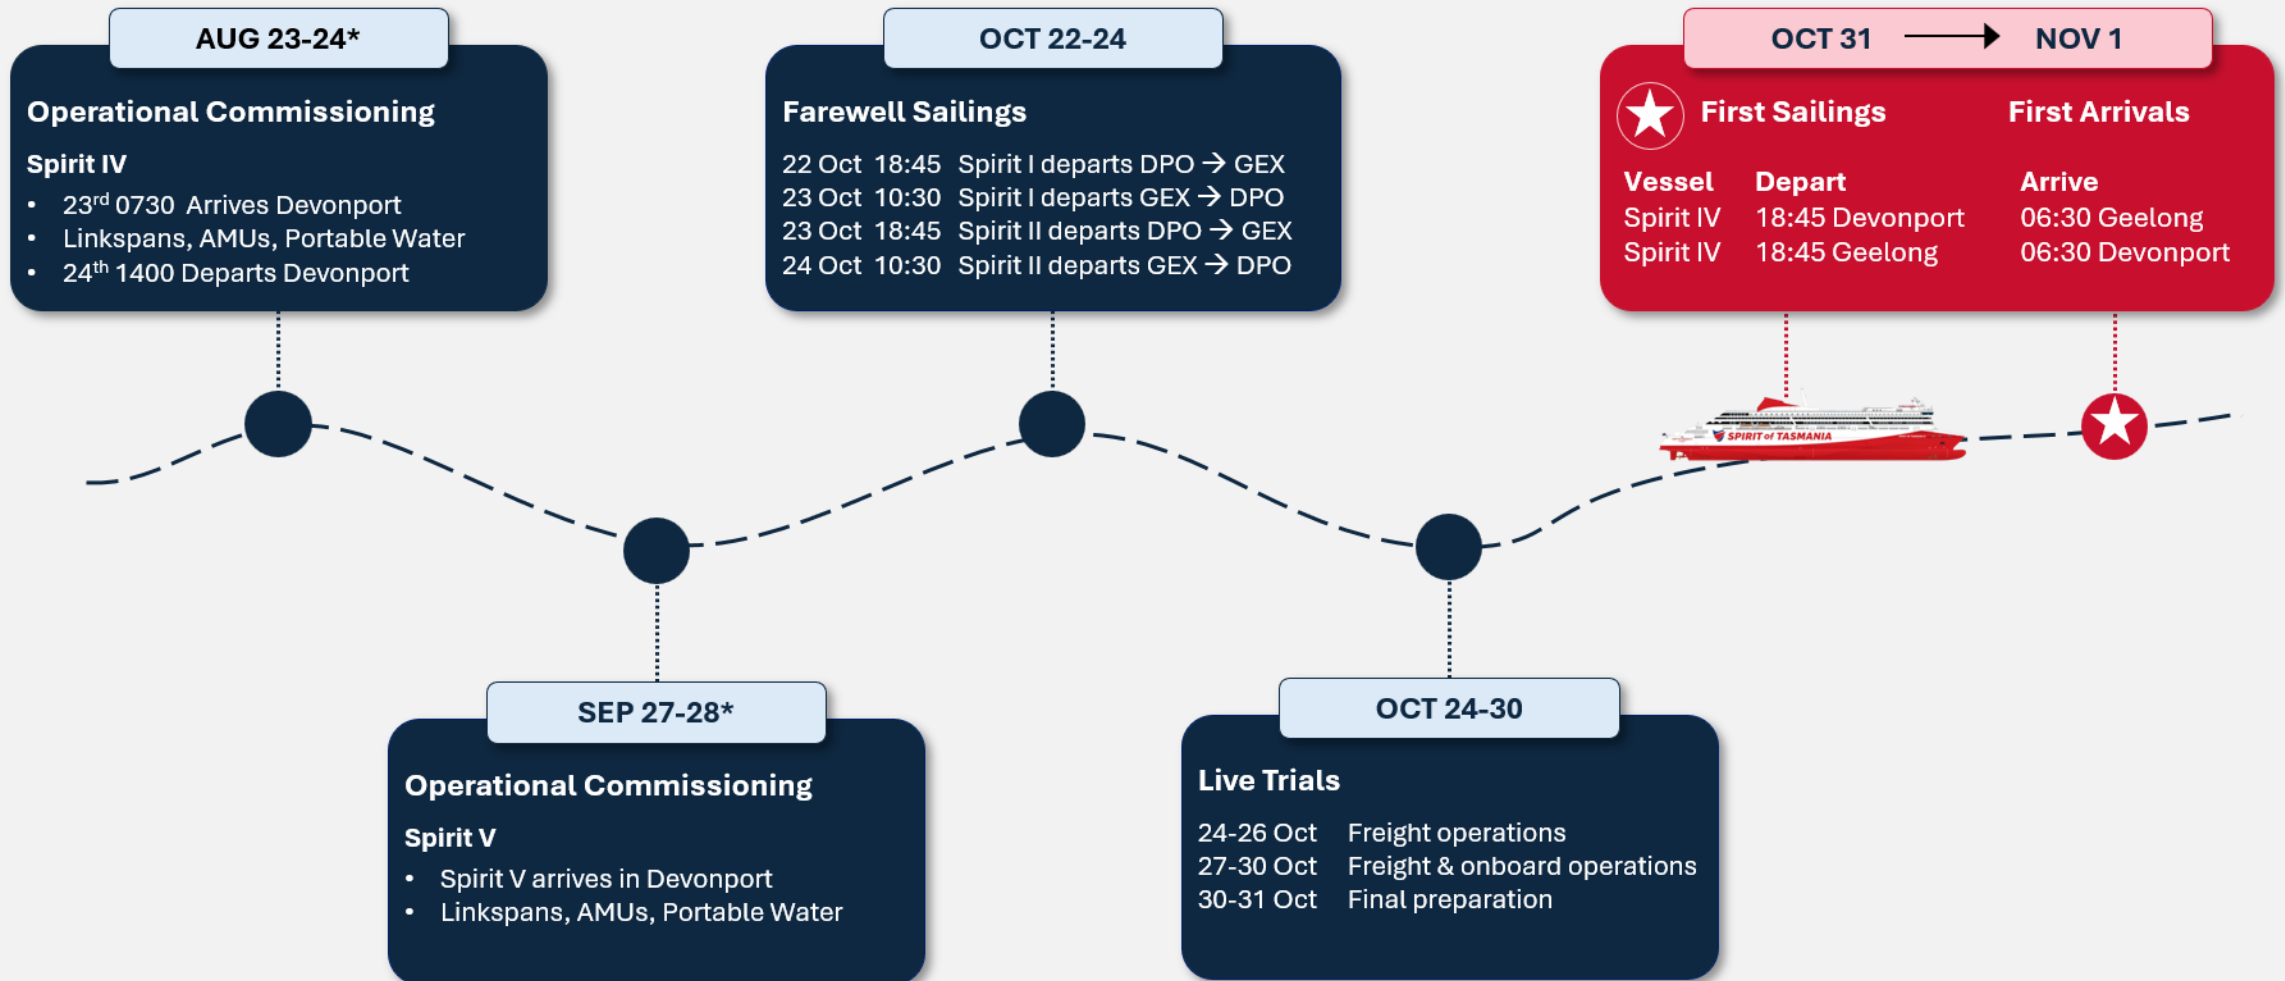

*Operational Commissioning commencing on August 23 is subject to weather conditions. The vessels will not be permitted entry into Devonport in severe, adverse weather. Wind speeds of over 20 knots will require a risk assessment to be performed between TT-Line and the Harbour Master. Should the vessel be unable to enter due to weather, another suitable time will be nominated. This will be on an alternative Sunday to Monday.

Operational Commissioning


23 - 24 August

Spirit Quay, Terminal 3 Devonport

Real-world testing, commissioning and training of the systems and equipment that connect our ships to our terminals.

During wet testing, we confirm each connection operates safely and reliably under operational conditions.


*Operational Commissioning commencing on August 23 is subject to weather conditions. The vessels will not be permitted entry into Devonport in severe, adverse weather. Wind speeds of over 20 knots will require a risk assessment to be performed between TT-Line and the Harbour Master. Should the vessel be unable to enter due to weather, another suitable time will be nominated. This will be on an alternative Sunday to Monday.

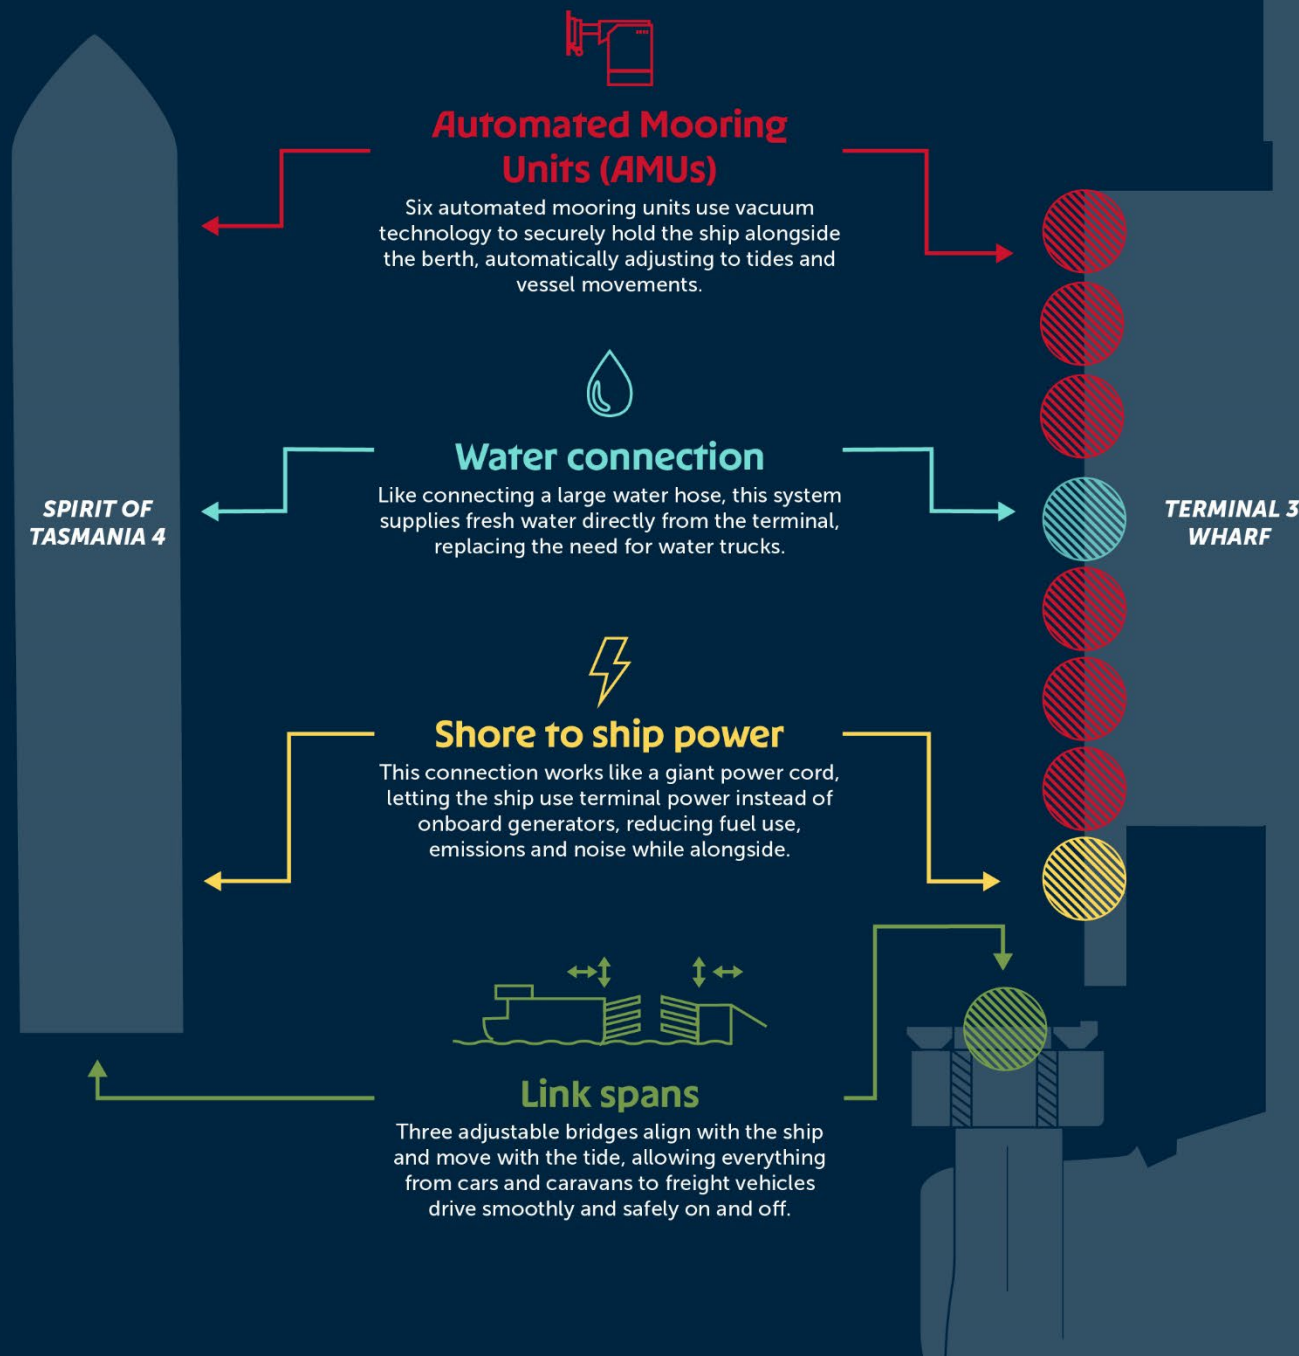

Live Trials

24th – 30th October

End-to-end testing across the entire passenger journey

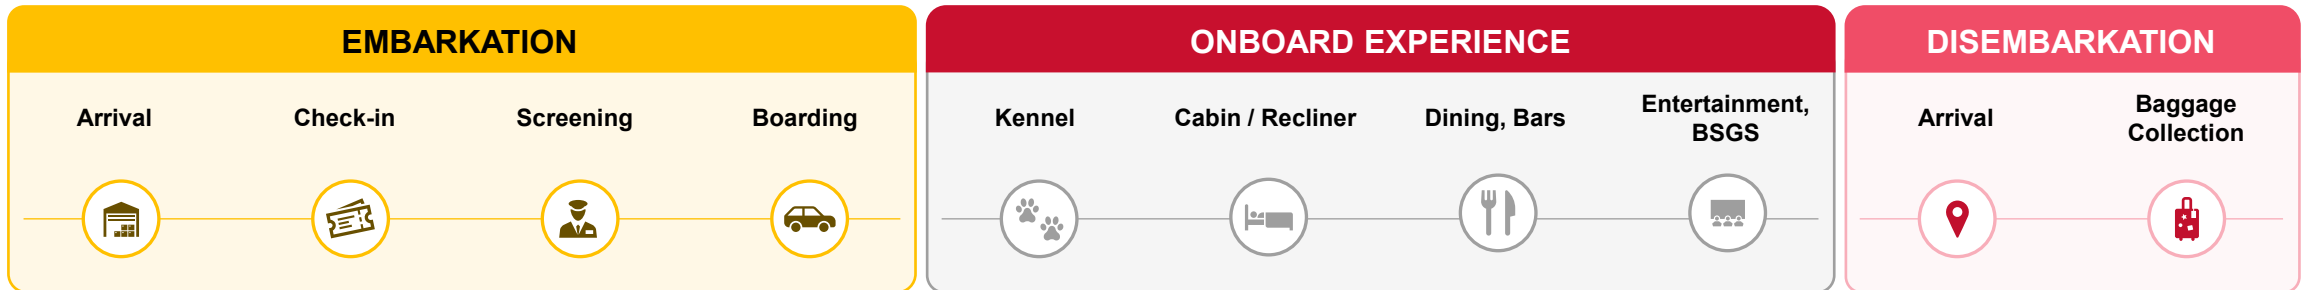

We will test every stage of the journey, from check-in through to arrival and disembarkation
